
107th & Military east to 105<sup>th</sup> & Military.

45 6 x6 posts,

47 4 x 4 posts total.

42 original, 3 replaced - 28 original, 19 replaced.

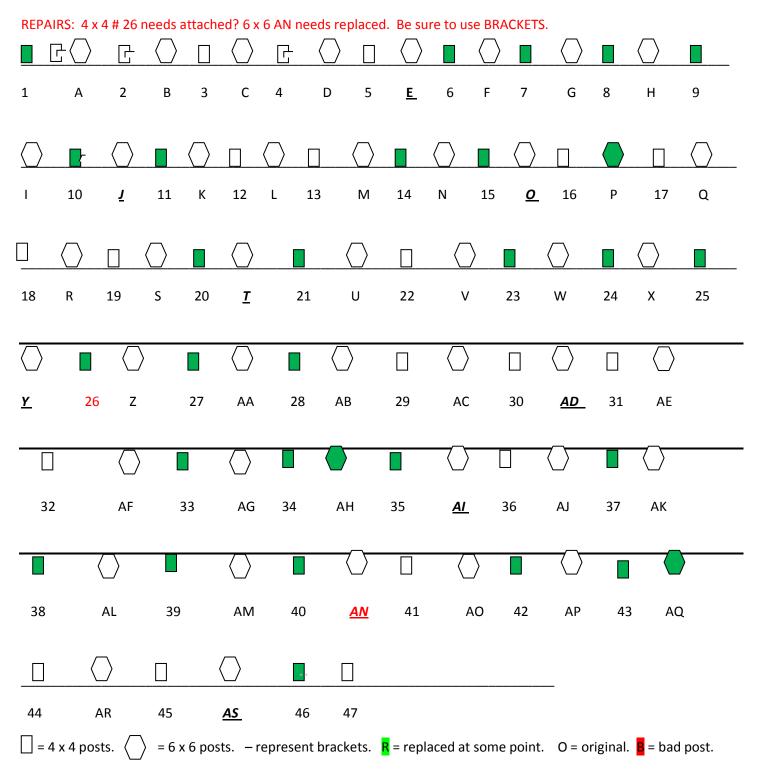

1. For every 6 x 6 post that is replaced be sure to put a bracket on each cross board instead of toe nail.

- 2. Be sure post is plumb and true.
- 3. Be sure to clean up after, no concrete pieces around and the dirt is spread out.
- 4. Crew only talks to the chairman of the grounds committee.
- 5. 6 x 6 Posts where the marking is highlighted, underscored and italicized are marked with a tack.
